Orange County Traffic Engineering

Conroy Windermere Rd at Hiawassee Rd

File Name : 011509 Conroy Windermere Rd at Hiawassee Rd PM TMC
Site Code : 00000000
Start Date : 1/14/2009

COUNTED BY: Arthur Woods

Page No : 1

Groups Printed- Unshifted
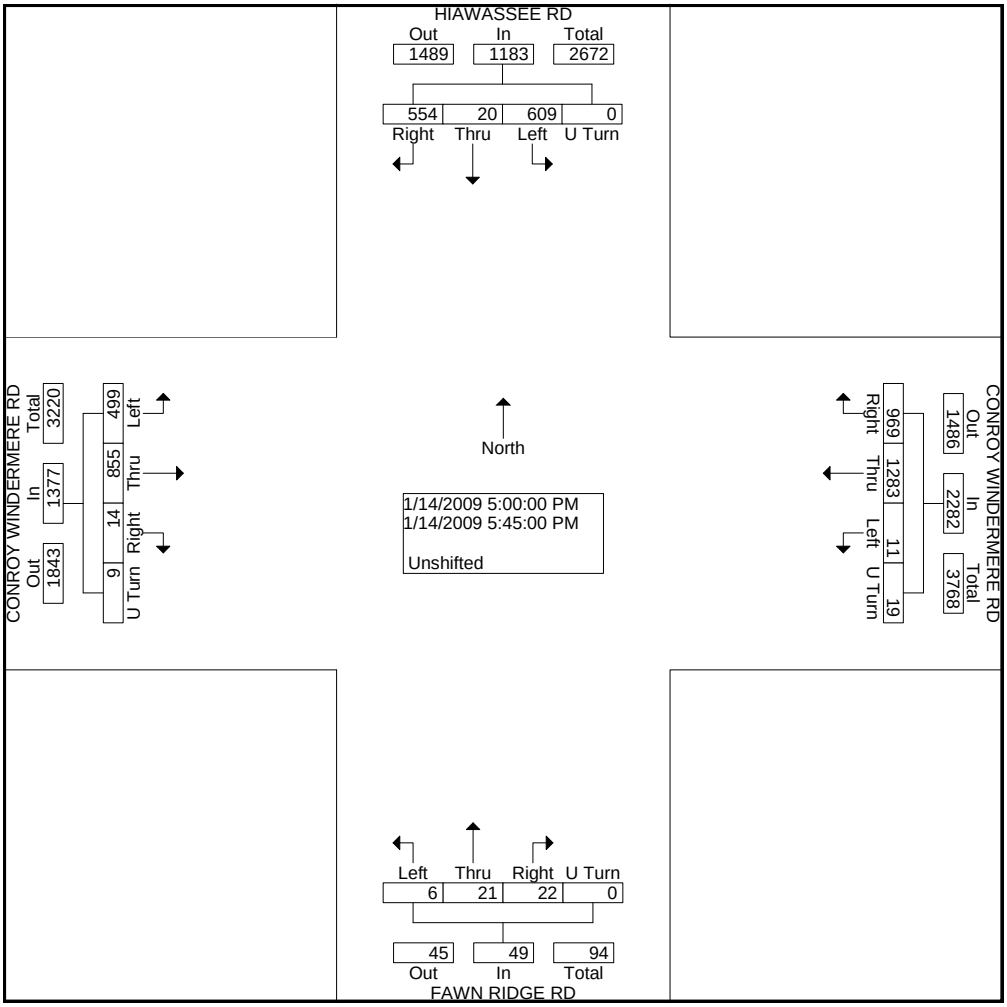
	HIAWASSEE RD From North				CONROY WINDERMERE RD From East				FAWN RIDGE RD From South				CONROY WINDERMERE RD From West				
Start Time	Right	Thru	Left	U Turn	Right	Thru	Left	U Turn	Right	Thru	Left	U Turn	Right	Thru	Left	U Turn	Int. Total
Factor	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	
05:00 PM	129	4	147	0	228	331	2	6	3	5	2	0	3	229	131	1	1221
05:15 PM	161	5	172	0	238	249	2	2	6	5	2	0	5	210	135	3	1195
05:30 PM	140	3	157	0	240	347	0	6	4	6	0	0	4	233	118	1	1259
05:45 PM	124	8	133	0	263	356	7	5	9	5	2	0	2	183	115	4	1216
Total	554	20	609	0	969	1283	11	19	22	21	6	0	14	855	499	9	4891
Grand Total	554	20	609	0	969	1283	11	19	22	21	6	0	14	855	499	9	4891
Apprch %	46.8	1.7	51.5	0.0	42.5	56.2	0.5	0.8	44.9	42.9	12.2	0.0	1.0	62.1	36.2	0.7	
Total %	11.3	0.4	12.5	0.0	19.8	26.2	0.2	0.4	0.4	0.4	0.1	0.0	0.3	17.5	10.2	0.2
